




ALAMO REGIONAL MOBILITY AUTHORITY COUNTY OF BEXAR



Project: Blanco Road Phase II – Non-Tolled (BC06)

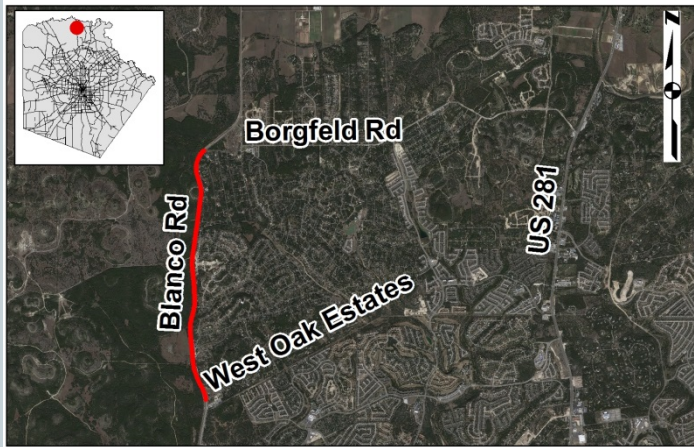

Limits: West Oak Estates Drive to Borgfeld Road.

Contractor: Harper Brothers Construction

Engineer: CP&Y, Inc.

Construction Cost: \$18,478,805.96

Construction NTP: 06/08/20

Contract Completion Date: 05/19/22

Projected Completion Date: 05/19/22

Scope: Expand from an existing two-lane rural roadway to a four-lane roadway consisting of two 12-foot travel lanes with six-foot shoulders in each direction, a raised median, curb and sidewalk on the northbound side.

Status: XX% Paid Out, XX% Time used

Monthly Activity:

- Mobilization and Prep-Right-of-Way

