




ALAMO REGIONAL MOBILITY AUTHORITY COUNTY OF BEXAR



Project: Talley Road Phase I – Non-Tolled (BC03)

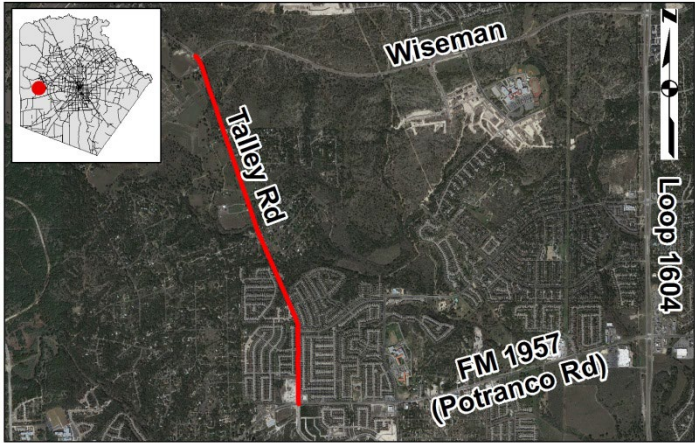

Limits: Potranco Road (FM 1957) to Wiseman Blvd.

Contractor: Texas Sterling Construction

Engineer: CP&Y, Inc.

Construction Cost: \$22,305,572.62

Construction NTP: 11/11/19

Contract Completion Date: 07/05/22

Projected Completion Date: 12/30/22

Scope: Expand from an existing two-lane rural roadway to a four-lane urban roadway consisting of two 12-foot travel lanes in each direction, a median, curb, and sidewalk.

Status: In Construction

